Launch & Marketing Playbook — DBR · W2SA · Lucent Veritas

Prepared: 2026-10-14 (Wed) · **For:** Sean (T0) · **Source:** Portfolio SITREP 2026-10-14 · **Times:** ET

0. Bottom line

- **New target: the marketing machine is running by Fri Oct 16 (Day 3), not ~Oct 26.**
  - All 5 "launched and marketing" criteria are green Friday at 16:00.
  - The weekly scorecard starts Mon Oct 19.
- **Why it can go faster than two weeks:**
  - Most open items are decisions, settings, and small fixes. Very little is real building.
  - Three lanes run in parallel: Sean, Claude, and Codex.
  - Sean's time is the only real limit, so his work is grouped into two short windows a day (~3.7 h Wed–Fri).
  - **Sat Oct 17 and Sun Oct 18 are work days** (~3 h of Sean's time). They're used to get ahead: P3 drafted, Facebook live, all of Week 1 queued.
  - Every decision has a recommended default. That way a slow answer doesn't stall the work.
- **The only long wait is Mailgun DNS verification** (it can take up to 48 h). So the DNS records go in **today**. There's also a fallback that needs no DNS at all (§7.3).
- **Don't wait on the social-post generator fix.** Claude writes the P1 posts by hand today. Codex fixes the generator in parallel, in time for P2.
- **Phones:** I ran a quick phone test of w2sa.online today. It found a concrete problem: a **6.3 MB intro video** behind a black screen. A one-hour hotfix (skip the intro on phones) clears it (§7.2).
- **The money path stays untouched while traffic ramps up.** For billing I recommend **Option B**: DBR only reads W2SA's Stripe account and changes nothing.

What changes vs. the SITREP plan

Milestone	SITREP plan	This playbook	Gain
First social post (P1 announcement)	This week (Oct 14–19)	**Thu Oct 15**	Locked to Day 1
W2SA works on phones	This week	**Thu Oct 15** hotfix · Fri full pass	2–4 days
Revenue visible in one place	This week (after decision)	**Fri Oct 16**	1–3 days
Audit-offer email can go out	This week	**Fri Oct 16** (1:1 fallback today)	1–3 days
All 5 "launched" criteria green	~Oct 26	**Fri Oct 16**	~10 days
P3 research (2 sourced facts)	Before Oct 23	**Fri Oct 16**	1 week
P3 creation	Oct 23	**Sat Oct 17**	6 days
P3 finished (ready for its Nov 5 launch)	Not set	**Wed Oct 21**	2 weeks of buffer
Second social channel (Facebook)	Not planned	**Sat Oct 17**	New
P2 publish	Oct 27	**Thu Oct 22**	5 days

Milestone	SITREP plan	This playbook	Gain
First audit-offer email to a list	Blocked (no email channel)	**Tue Oct 20**	Unblocked
P1 snippet wave 1 (hard date)	Oct 20	**Oct 20, kept**, queued by Fri	On time, no scramble

1. The funnel we're switching on

From the live sites, the money path is:

1. **Lucent Veritas paper**: P1, *The 2027 Small Business Digital Readiness Report*.
2. **Social post**: LinkedIn post, snippet card, or carousel.
3. **P1 page on lucentveritas.com**, which needs a visible CTA to the next step.
4. **W2SA free Digital Health Check**: `w2sa.online/digital-health-check`. Each submission creates a lead in the DBR CRM.
5. **Paid W2SA Diagnostic Dossier**: 199–1,200, paid through Stripe.
6. **Fix My Website** (500–4,000) or **Replace My Website** (2, 250–6,500).

- Side path: LV commissioned white papers, booked through the Cal.com `lv-white-paper-planning` link.
- Every step needs three things:
  - A link with UTM tags (§7.6).
  - A page that works on a phone (§7.2).
  - A number on the weekly scorecard (§7.6).
- **Check today (15 min):** does the P1 page clearly link to the W2SA Digital Health Check? If it doesn't, social traffic dead-ends on the paper. This is the cheapest fix in the whole plan.

2. Decisions — answer today

- Reply with just the numbers you **disagree** with. Anything unanswered by **9:00 Thu Oct 15** takes the default.
- D1–D5 keep the SITREP's order. D6–D8 are new.

#	Decision	Recommended default	Why	Unblocks
D1	W2SA revenue visibility	**Option B**: DBR's dashboard reads W2SA's Stripe account through a read-only restricted key	Doesn't touch the live checkout while we drive traffic. Takes hours, not days. Easy to undo. Option A can come later if it's still needed.	Gate 2
D2	Social channels & posting	**LinkedIn now**: Sean's personal profile is the main voice, the LV and W2SA company pages repost. **Facebook (W2SA page) from Sat Oct 17.** X and Instagram wait. Post by hand Thu–Fri, then queue each week in LinkedIn's built-in scheduler (or one tool such as Buffer or Postiz to cover both channels).	The paper → LinkedIn rhythm is already the plan. Personal profiles usually reach far more people than company pages. Small-business owners are heavy Facebook users.	Gate 3, the whole social lane
D3	Set up Mailgun now?	**Yes, today.** Send from a subdomain such as `mg.w2sa.online`.	Your condition for restarting it is met. The DNS wait is the longest item in the plan.	Gate 4

#	Decision	Recommended default	Why	Unblocks
D4	Full Build Factory	**Commit and push P1–P3 today. Commit a tested P4 checkpoint by Fri Oct 16. Then pause** (unless Billy's is a paying job — Sean confirms).	Protects work that only exists locally right now. Frees up Codex.	Codex lane
D5	Freeze	**Confirm the freeze:** LUVK, NCC remediation, Amatrix/HRC/HAWL, new Nexus agent work	Rule: if it doesn't get a post out, convert a visitor, or make revenue visible, it waits.	Focus
D6	Which brand sends the email	**W2SA**, signed by Sean. The LV paper is the hook.	The audit offer is a W2SA product, and its buyers are small businesses.	Email copy
D7	Dormant projects	**Archive** SITREP Intelligence, Knowledge Engine, and the WP_Distribution video build (manual posting replaces it). **Keep** the HAWL/Amatrix/HRC playbooks as frozen documents.	Clears noise. Nothing is lost.	Can wait until Fri
D8	Post approval rule	**Sean approves the first 3 posts. After that, posts built from approved templates go out unless Sean vetoes them in the queue.**	Keeps Sean from becoming the bottleneck once the cadence is running.	Steady-state cadence

3. Operating rules for the sprint

- **The freeze test:** does this get a post out, convert a visitor, or make revenue visible? If not, it waits.
- **Frozen:** LUVK (v1 and v2), the LUVK local-AI switch, NCC remediation, Amatrix/HRC Stripe accounts, the `dbr_projects` table, EASS judge wiring, the LV multi-tenant vault, NDRS, voice/narration, and new Nexus agent work.
- **Allowed small builds, because they feed the funnel:**
  - W2SA phone fixes.
  - Option B billing view.
  - Mailgun wiring plus an opt-in form.
  - Snippet-card template.
  - Social-generator fix.
  - Product-lookup letter-case fix.
- **NCC alert noise:** it has reported 2 critical issues every 48 h for 7 weeks.
  - Spend 10 minutes confirming neither issue touches a live system (DBR, W2SA, LV).
  - If neither does, mute the alert until NCC is unfrozen.
- **Sean's time windows:**
  - **9:00–9:30**: approve and post.
  - **16:00–16:30**: review and decide.
  - Everything else comes to Sean as a short async item with a recommended answer.
- **Manual first, automate second.** Post natively Thu–Fri. From Week 1 on, the week's posts are queued in advance: Sun Oct 18 for Week 1, then every Friday.
- **Protect work:** all uncommitted work gets committed and pushed today: WP Factory, LV, and Full Build Factory P1–P4.

4. Lanes & owners

- **Sean (T0)**: decisions, account access, DNS records, Stripe dashboard checks, Anthropic key rotation, real-phone tests, approving and posting.
- **Claude**:
  - W2SA phone fixes.
  - Option B billing view.
  - Mailgun wiring, email template, opt-in form.
  - P1 post copy and snippet-card template.
  - UTM links, analytics, and scorecard.
  - Security cleanup in code.
  - DBR small fixes.
- **Codex**:
  - P2 check and QA.
  - Social-generator fix with a guard test.
  - P1 and P2 social packs.
  - P3 research and creation.
  - Commit and push all WIP.
  - Full Build Factory checkpoint, then pause.

5. Day-by-day sprint (Oct 14–16): "Ignition"

Launch & Marketing Sprint · Oct 14 – Oct 23, 2026

DBR · W2SA · Lucent Veritas — prepared for Sean (T0). All times ET. Sat Oct 17 and Sun Oct 18 are work days.

MACHINE RUNNING	SITREP TARGET	SEAN'S TIME WED–FRI	SEAN'S TIME SAT–SUN
Fri Oct 16	~Oct 26	~3.7 h	~3.1 h

Sprint view

three lanes in parallel; the top row is what the public sees

Decisions / ops · Social · W2SA mobile · Email · Billing · Papers · Tracking · Security · Gate / milestone

	Wed Oct 14 Day 0 · Decide & unblock	Thu Oct 15 Day 1 · First post, phones fixed	Fri Oct 16 Day 2 · Machine running	Sat Oct 17 Day 3 · Get ahead	Sun Oct 18 Day 4 · Queue the week	Mon Oct 19 Tracking starts	Tue Oct 20 Hard date	Wed Oct 21 Wednesday	Thu Oct 22 Thursday	Fri Oct 23 Friday
What the market sees Posts & emails		SOCIAL ★ P1 announcement	SOCIAL P1 carousel	SOCIAL Facebook page goes live	SOCIAL First Facebook post	SOCIAL W2SA proof post	SOCIAL ★ P1 snippet wave 1 EMAIL ★ Audit-offer email #1	SOCIAL P2 teaser + P1 snippet	PAPERS ★ P2 publish + breakdown	SOCIAL P1 snippet
Sean (T0) Decide · approve · post	DECISIONS / OPS Answer decisions D1–D8 (15m) EMAIL Mailgun domain + DNS (20m) BILLING Stripe webhook check (10m) SOCIAL LinkedIn admin access (10m)	SOCIAL 9:00 approve & post (20m) W2SA MOBILE Real-phone test (15m) PAPERS 16:00 review P2 (30m)	SOCIAL 9:00 post carousel (10m) SECURITY 10:00 security hour (60m) PAPERS Confirm P3 facts (10m) GATE / MILESTONE **16:00 gate review (20m)**	SOCIAL Facebook page setup (30m) EMAIL Warm-contact list (30m) PAPERS Paper scoring + keep/archive (45m)	SECURITY Tunnel-token rotation (30m) SOCIAL Approve Week 1 queue (20m) PAPERS First-pass P3 review (30m)	TRACKING Scorecard #1 (15m)	EMAIL Approve the email send (10m)	SOCIAL 9:00 post (10m) PAPERS P3 line edits (30m)	PAPERS Publish approval (15m)	TRACKING Week recap (10m)
Claude Build · write · wire	SOCIAL Draft P1 post + snippets W2SA MOBILE W2SA phone hotfix PR TRACKING UTM sheet + analytics TRACKING P1 page → W2SA CTA	W2SA MOBILE Ship phone hotfix BILLING Billing Option B build EMAIL Mailgun wiring + opt-in SOCIAL Snippet-card template	BILLING Option B live + reconcile EMAIL Mailgun verified + test TRACKING Scorecard + baseline SOCIAL Queue Tue snippet wave	W2SA MOBILE Mobile intro cut ≤1.5 MB DECISIONS / OPS Product lookup case fix SOCIAL Render Week 1 cards W2SA MOBILE LV + P1 page phone pass	SOCIAL Queue Week 1 posts EMAIL Schedule email #1 TRACKING Pre-fill scorecard DECISIONS / OPS Portal + LV freeze check	TRACKING Fix anything the scorecard flags	EMAIL Send + watch delivery	TRACKING P2 page CTA + UTM check	W2SA MOBILE Phone check of the P2 page	SOCIAL Queue Week 2 SOCIAL Render P2 cards + carousel
Codex Papers · generator · commits	PAPERS Confirm P2 ran + QA SECURITY Commit & push all WIP SOCIAL Start generator fix PAPERS P3: source 2 facts	SOCIAL Generator fix + guard test SOCIAL Regenerate P1 social pack PAPERS P3 facts drafted DECISIONS / OPS Build Factory P4 checkpoint	PAPERS P2 fixes from review SOCIAL P2 social pack DECISIONS / OPS Build Factory → pause	PAPERS ★ P3 creation PAPERS P2 final + teaser assets	PAPERS P3 QA checks PAPERS Apply Sean's P3 notes	PAPERS P3 revisions	PAPERS P2 publish prep	PAPERS P3 final	PAPERS Publish P2 to LV	SOCIAL P2 social pack polish
Gate Done when	GATE / MILESTONE **Decisions in · DNS added · webhook confirmed · no local-only work**	GATE / MILESTONE **P1 posted · W2SA passes on real phones · Option B shows data**	GATE / MILESTONE **★ MACHINE RUNNING — 5/5 gate criteria green**	GATE / MILESTONE **P3 drafted · P2 final · Facebook live · Week 1 cards ready**	GATE / MILESTONE **Week 1 queued · tunnel rotated · P3 first review done**	GATE / MILESTONE **Weekly tracking live**	GATE / MILESTONE **Email channel proven**	GATE / MILESTONE **P3 done — two weeks ahead of launch**	GATE / MILESTONE **P2 live 5 days early**	GATE / MILESTONE **Week 2 queued**

Day 0 — Wed Oct 14 (today): decide & unblock

- **Sean (~55 min)**
- [ ] Answer D1–D8 (§2). 15 min.
- [ ] Mailgun: add the sending domain (`mg.w2sa.online`) and put the DNS records it shows into your DNS provider. 20 min. **Starts the propagation clock.**
- [ ] Stripe dashboard → Webhooks → the live endpoint. Confirm recent deliveries returned 2xx. 10 min. **Closes the 08-22 Sentinel P0 question.** If deliveries are failing, stop and fix that first: it's revenue.
- [ ] LinkedIn: confirm you're an admin on the LV and W2SA company pages (create either page if it's missing). 10 min.
- **Claude**
- [ ] Draft the P1 announcement and breakdown post, plus 6–8 snippet lines, by hand from the P1 paper. Templates are in Appendix A.
- [ ] Open the W2SA phone hotfix PR: skip the intro on phones and make the skip button bigger (§7.2).
- [ ] Build the UTM link sheet (§7.6). Confirm analytics records UTM-tagged visits on both sites.
- [ ] Check that the P1 page has a clear CTA to the W2SA Digital Health Check, with UTM tags.
- **Codex**
- [ ] Confirm P2 generated at 09:00 ET and run its quality checks. Flag it for Sean's review.
- [ ] Commit and push all uncommitted work: WP Factory, LV, and Full Build Factory P1–P4 branches.
- [ ] Start the social-generator fix (already defined in the WP Factory sitrep).
- [ ] P3: find two facts with primary sources.
- **Done when:** decisions are in, DNS records are added, the webhook is confirmed healthy, and no work exists only on a local machine.

Day 1 — Thu Oct 15: first post, phones fixed

- **Sean (~65 min)**
- [ ] **9:00** Approve and post the **P1 announcement** on LinkedIn (personal profile), then repost it from the LV page. 20 min.
- [ ] Real-phone test after the hotfix ships (checklist in §7.2). 15 min.
- [ ] **16:00** Review P2. 30 min.
- **Claude**
- [ ] Ship the phone hotfix and re-test on phones. (The mobile cut of the intro moves to Sat.)
- [ ] Build the Option B billing view (§7.4).
- [ ] Mailgun wiring: audit-offer email template, unsubscribe handling, and an opt-in on the P1 page and the Health Check form (§7.3).
- [ ] Snippet-card template, rendered from code (4:5, 1080×1350). No Canva time needed from Sean.
- **Codex**
- [ ] Land the social-generator fix plus a guard test (§7.5). Regenerate the P1 social pack and compare it with Claude's hand-written version.
- [ ] Draft the P3 facts with sources.
- [ ] Full Build Factory: commit a tested P4 checkpoint.
- **Done when:** P1 is posted, W2SA passes on a real iPhone and Android (including inside the LinkedIn app), and the Option B view shows data.

Day 2 — Fri Oct 16: machine running

- **Sean (~100 min)**
- [ ] **9:00** Post the **P1 carousel** (a LinkedIn document post). 10 min.
- [ ] **10:00** Security hour with Claude (§7.7). 60 min.
- [ ] Confirm the P3 facts. 10 min.
- [ ] **16:00** Gate review against §10. 20 min.
- **Claude**
- [ ] Turn on Option B. Reconcile one week of W2SA charges against the Stripe dashboard.
- [ ] Mailgun domain verified. Send a test of the audit-offer email to Sean, then fix anything that renders badly.
- [ ] Scorecard live with baseline numbers (§7.6).
- [ ] Queue next week's posts. P1 snippet wave 1 is set for Tue Oct 20.
- **Codex**
- [ ] Apply the P2 fixes from Sean's review. Build the P2 social pack with the fixed generator.
- [ ] Full Build Factory committed and tested → **pause**.
- **Done when:** all 5 gate criteria are green (§10).

Day 3 — Sat Oct 17: get ahead

- LinkedIn stays quiet (weekend reach is low). The weekend is for building the buffer.
- **Sean (~1.75 h)**
- [ ] Set up the Facebook W2SA page: cover image, About text from w2sa.online, and a button to the free Health Check (`utm_source=facebook`). 30 min.
- [ ] Warm-contact list: pick 20–30 people from the DBR CRM and your inbox for email #1. Mark who should get a 1:1 note instead. 30 min.
- [ ] Paper scoring checks and keep/archive for the 20 older papers (pulled forward from the week of Oct 26). 45 min.
- **Claude**
- [ ] Mobile cut of the W2SA intro: portrait, 720p H.264, ≤1.5 MB, with a poster frame (moved from Thu).
- [ ] Product-lookup fix: compare brand keys in lowercase, plus one test (moved from Thu).
- [ ] Render P1 snippet cards 4–8 and the P2 teaser card, so Week 1 has all its graphics.
- [ ] Phone pass on lucentveritas.com and the P1 page (same checks as W2SA).
- **Codex**
- [ ] **P3 creation** with the confirmed facts (was Oct 23).
- [ ] P2 final copy, teaser excerpt, and 3 pull-quotes (was Tue Oct 20).
- **Done when:** P3 is drafted, P2 is final, the Facebook page is live, and Week 1's cards are ready.

Day 4 — Sun Oct 18: queue the week

- **Sean (~1.3 h)**
- [ ] Tunnel-token rotation with Claude, in Sunday's low-traffic window (§7.7). 30 min.
- [ ] Approve the whole Week 1 queue: every post Mon–Fri plus Tuesday's email. 20 min.
- [ ] First-pass P3 review: big-picture notes only. Line edits come Wed. 30 min.
  - Public: the first Facebook post on the W2SA page ("A website can look fine and still lose customers...").
- **Claude**

- [ ] Queue Week 1 in LinkedIn's scheduler: Mon proof post, Tue snippet wave 1, Wed teaser + snippet, Thu P2 launch, Fri snippet.
- [ ] Schedule email #1 for Tue 9:30 (or put 1:1 drafts in Sean's inbox if Mailgun isn't verified).
- [ ] Pre-fill the scorecard with Fri–Sun numbers so Monday's review takes 15 minutes.
- [ ] Check the client portal's public address. Confirm with Codex that the LV deploy freeze is lifted, and note it in the LV sitrep (moved from Wed).

- **Codex**
- [ ] Run the quality checks on P3 (was Wed Oct 21). Apply Sean's first-pass notes.
- **Done when:** Week 1 is fully queued, the tunnel token is rotated, and P3 has had its first review.

---

6. Week 1 (Oct 19–23): run the cadence

- The whole week was queued and approved on Sunday, so Sean's time drops to ~1.5 h.
- **Mon Oct 19**
  - Scorecard #1 (Sean, 15 min).
  - Public: **W2SA proof post** on LinkedIn and Facebook, a finding from the sample report (e.g., "contact form fails on mobile").
  - Claude: fix anything the scorecard flags.
  - Codex: finish the P3 revisions from Sunday's notes.
- **Tue Oct 20 — hard date**
  - Public: ★ **P1 snippet wave 1** and **audit-offer email #1**.
  - Sean approves the send (10 min). Claude sends it and watches bounces and unsubscribes.
  - Codex: P2 publish prep (LV page, metadata, PDF, CTA block).
- **Wed Oct 21**
  - Public: **P2 teaser** and a P1 snippet.
  - Sean: P3 line edits (30 min).
  - Claude: check the P2 page CTA and UTM tags.
  - Codex: **P3 final**, two weeks ahead of its Nov 5 launch.
- **Thu Oct 22**
  - Public: **P2 publish + breakdown post** (was Oct 27).
  - Claude: phone check of the P2 page.
- **Fri Oct 23**
  - Public: a P1 snippet.
  - Sean: 10-min week recap.
  - Claude: queue Week 2 and render the P2 cards and carousel.

---

7. Workstream runbooks


7.1 Social distribution

- **Channels (D2 default):**
  - LinkedIn: Sean's personal profile is the main voice. The LV and W2SA company pages repost.
  - Facebook: W2SA page live Sat Oct 17, first post Sun Oct 18.

    - X and Instagram: parked until the scorecard shows LinkedIn working.
- **Post types:**
    - **Announcement/breakdown**: hook, 3 findings, the "so what," then a CTA. 150–250 words.
    - **Snippet**: one stat or finding on a 1080×1350 card, plus 2–3 lines of copy and a CTA.
    - **Carousel**: a 6–10 slide PDF uploaded as a LinkedIn document post, 1080×1350 per slide.
    - **W2SA proof post**: one common website problem, why it costs customers, and a link to the free check.
- **Links:**
    - Every link carries UTM tags (§7.6).
    - Test both placements: link in the post body vs. link in the first comment. Keep whichever gets more clicks on the scorecard.
- **CTA:** the primary CTA is the **W2SA free Digital Health Check**. The secondary CTA is reading the full paper.
- **Posting steps (manual, week 1):**
    - Post from Sean's profile at 9:00 ET on weekdays.
    - Repost from the company page within an hour.
    - Reply to every comment the same day.
- **From Week 1:** the week's posts are queued ahead in LinkedIn's built-in scheduler (Sun Oct 18 for Week 1, then each Friday) and Sean approves the queue. If posting to two channels gets tedious, move to one scheduling tool.
- **Graphics:**
    - Claude renders snippet cards and carousels from one code template, so they stay on-brand at no extra cost.
    - Canva stays available for one-off edits.

7.2 W2SA mobile pass

- **What I found today:** a phone simulation on a desktop test browser (emulated iPhone 13 at 390×664 and Pixel 7 at 412×839). This is **not** a substitute for a real phone.
    - **The intro video `intro-reveal.mp4` is 6.3 MB** (6,275,995 bytes). There's one version, no poster image, and phones download all of it. That's ~93% of the homepage's 6.4 MB load.
        - That's roughly **5 s on a 10 Mbps connection and 12+ s on a weak 4 Mbps signal.**
    - While the video loads, a phone shows a **full-screen black overlay with only "Skip intro"** on it. Social visitors decide in seconds.
    - **"Skip intro" is ~98×38 px with 14 px text.** That's below the 44×44 px minimum tap size.
    - The video uses `object-fit: cover` on a tall portrait screen. A landscape video gets its sides cropped heavily, which is likely the "intro crop" issue. Confirm on a real phone.
    - **Good:** when the video can't play, the intro closes itself after ~3.4 s and the page works. There's no sideways scrolling at 390 or 412 px.
    - **Minor:** the header "Review My Site" button wraps onto two lines at 390 px, and the logo loads as a 260 KB image.
    - **Limit:** the test browser can't play this video format (H.264), so I couldn't see the animation itself. The real-phone test is still required.

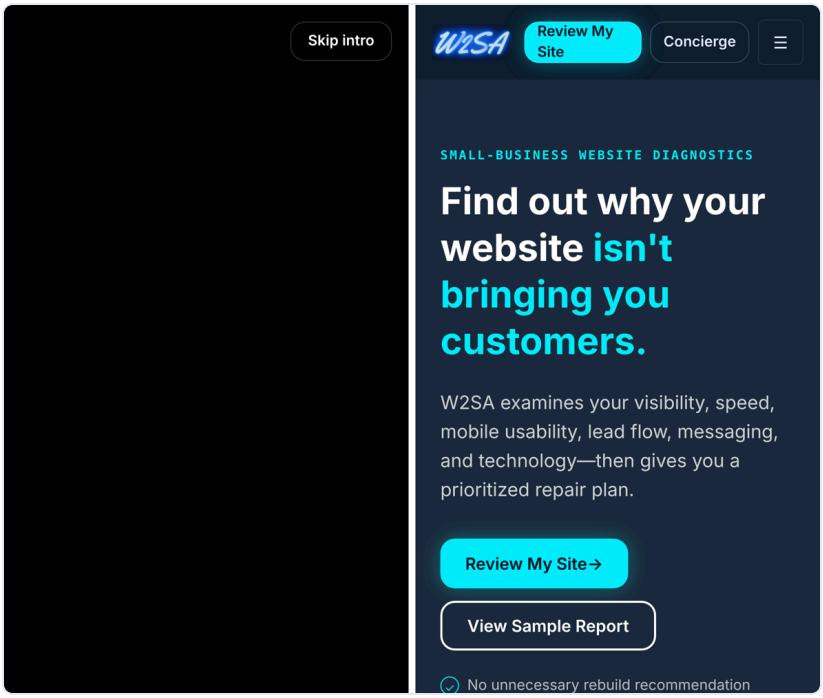

- **Fixes, in order:**
  1. **Hotfix (≤1 h):** on screens ≤768 px wide, or when the visitor has Data Saver on or reduced motion set, skip the intro and show the hero straight away. Until a mobile cut exists, the intro runs on desktop only.
  2. **Skip button:** make it at least 44 px tall, keep it clear of the iPhone notch area (`env(safe-area-inset-top)`), and give it higher contrast.
  3. **Mobile cut:** a 9:16 or 4:5 version at 720p, H.264, **≤1.5 MB**, with a poster frame and `preload="metadata"`. Turn the intro back on for phones only if it still loads fast.
  4. **Header CTA:** use the short "Review Site" label below 400 px.
  5. **Logo:** serve a correctly sized WebP/AVIF (aim for under 40 KB).
- **Real-phone test checklist (Sean, 15 min):**

- [ ] iPhone Safari and Android Chrome.
- [ ] **LinkedIn in-app browser**: tap your own post's link. Social clicks open here, not in Safari or Chrome.
- [ ] Facebook in-app browser (from Sun Oct 18).
- [ ] First screen appears in under 3 s on cellular with Wi-Fi off.
- [ ] Tap "Review My Site," submit the Digital Health Check, and confirm the lead shows up in the DBR CRM.
- [ ] Open the Dossier checkout and confirm the Stripe page loads (no purchase needed).
- [ ] Repeat for lucentveritas.com and the P1 page.

7.3 Email channel (Mailgun)

- **Setup:**

- [ ] Add the sending subdomain `mg.w2sa.online` in Mailgun (Day 0).
- [ ] Add the DNS records Mailgun shows, typically SPF (TXT), DKIM (TXT), two MX records, and a tracking CNAME (Day 0).
- [ ] Add DMARC on the root domain, starting at `p=none`: `_dmarc.w2sa.online TXT "v=DMARC1; p=none; rua=mailto:<you>"`. Gmail and Yahoo expect authenticated mail and easy unsubscribe.
- [ ] Confirm the Mailgun plan can send to your list. Trial and sandbox setups only send to approved addresses.
- [ ] Click verify in Mailgun. It can take minutes or up to 48 h.

- **Who gets the email (consent matters):**
  - The current Health Check consent covers "prepare my free preliminary diagnostic and follow up about it." **It does not cover marketing email.**
    - Add an **optional, unticked** box: "Send me the 2027 readiness report and occasional tips."
  - Add the same opt-in to the P1 page ("Email me the report + checklist").
  - Existing warm contacts in the DBR CRM: start with **1:1 personal emails**, not a bulk send.
- **Compliance (CAN-SPAM):** every email needs:
  - A real sender.
  - An honest subject line.
  - A postal address.
  - A working unsubscribe link (Mailgun's `%unsubscribe_url%`), honored promptly.
- **Warm-up:** keep early sends small, in the dozens. Watch the bounce rate and complaints before sending more.
- **Fallback if DNS isn't verified by Friday:** Sean sends the audit-offer email as personal 1:1 messages from his own inbox to 20–30 warm contacts. That needs no setup, can start today, and personal emails usually convert better anyway.
- **Draft email:** Appendix B.

7.4 Billing visibility — Option B

In **W2SA's** Stripe account, create a **restricted key with read-only access** to Charges, Payment Intents, Checkout Sessions, and Balance Transactions.

Store it in DBR's secrets (e.g., `STRIPE_W2SA_READ_KEY`). Never put it in a repo or an `.env.example` file.

DBR pulls W2SA payments on a schedule, or adds a `checkout.session.completed` webhook in W2SA's account pointing at DBR. Tag these payments `source=brand-nexus`.

No double counting: match on Stripe object IDs. Charges dbr-api already records must not appear twice.

- **Done when:** one known brand-nexus W2SA charge from the last 30 days appears in DBR with the right amount, and the weekly total matches the Stripe dashboard.
- **Later, only if two reporting sources become a problem:** Option A, routing brand-nexus charges through DBR. That's a change to the money path, so it waits until after launch.

7.5 Papers and the social generator

- **P2:** confirm it generated today at 09:00 ET and passed QA. Sean reviews Thu. Fixes Fri. **Publish Thu Oct 22.**
- **P1 social generator:**
  - Codex applies the fix already defined in the WP Factory sitrep.
  - **Add a guard test so the bug can't come back.** It fails if the output is shorter than ~300 characters, matches the slug, or is missing the hook, the 3 points, or the CTA link.
- **P3:**
  - Codex finds the two facts by Thu. Sean confirms Fri.
  - **Creation moves to Sat Oct 17.** If the schedule is automated and can't move, run it by hand — the point is that P3 is no longer blocked.
  - QA and Sean's first-pass review Sun Oct 18. Line edits and **P3 final Wed Oct 21**. Teaser Tue Nov 3. **Publish Thu Nov 5 (proposed).**
- **Human scoring checks and old-paper keep/archive decisions:**

- One 45-min session on Sat Oct 17 (pulled forward from the week of Oct 26).
- Kept papers become the **evergreen recycle** library for Thursday slots.

7.6 Tracking & the weekly scorecard

- **UTM convention:**
  - `utm_source` = `linkedin` | `facebook` | `email`
  - `utm_medium` = `social` | `email`
  - `utm_campaign` = `p1-readiness-2027` | `p2-<slug>` | `p3-<slug>` | `audit-offer`
  - `utm_content` = `announce` | `snippet-01…` | `carousel` | `proof-01…` | `email-01…`
  - Example: `https://w2sa.online/digital-health-check?utm_source=linkedin&utm_medium=social&utm_campaign=p1-readiness-2027&utm_content=announce`
- **Analytics:** confirm both sites record visits by UTM.
  - A quick scan of the LV homepage and its main script found no common analytics tag.
  - If none is present, add a lightweight one (Cloudflare Web Analytics, Plausible, or GA4) on Day 1.
- **Scorecard (Mondays, 15 min, starting in a Google Sheet):**

Metric	Source
Posts shipped vs. planned	Calendar
Impressions, clicks, new followers	LinkedIn analytics
Site visits from social and email (by UTM)	Analytics
Digital Health Check submissions	DBR CRM
Bookings (LV + W2SA)	Cal.com
Checkouts and revenue (both Stripe accounts)	DBR (after Option B)
Emails sent, opened, clicked, unsubscribed, bounced	Mailgun

- **First-month guardrails** (adjust after the Oct 19 baseline):
  - At least 4 posts a week, shipped on schedule.
  - At least one Digital Health Check submission a week by the end of October.
  - Bounce rate under 2% and complaint rate near zero.

7.7 Security hour (Fri Oct 16, 10:00–11:00, Sean + Claude)

- **Order matters.** The n8n workflows produce papers, so the key has to move **before** the old one is revoked. Doing it after P2 and before P3 creation avoids breaking a paper run.
  1. [ ] Create a new Anthropic API key in the console.
  2. [ ] In n8n, store it as a **credential** and switch WF-101 to WF-105 to use that credential. Run each workflow once and confirm it works.
  3. [ ] Change `white_papers\deploy_n8n_workflows.py` to read the key from an environment variable. Delete line 21's literal key. Commit.
  4. [ ] **Revoke the old key**, then re-run one workflow. *Deleting the key from the file doesn't remove it from git history. Revoking it is what closes the exposure.*
  5. [ ] Replace the Stripe test key in LV's `.env.example` with a placeholder (`sk_test_xxx`).

6. [ ] **Sun Oct 18, low-traffic window:** rotate the tunnel token in `lv-tunnel-config.yml`, then check right away that lucentveritas.com still loads. Have a rollback ready. A bad rotation takes LV offline, so it goes in the quietest slot, when you're both working.

7.8 DBR cleanup (small, allowed)

- Product-lookup letter-case mismatch: compare in lowercase plus one test (Day 1).
- Client portal public address: open it and confirm the HTTP status (Day 0).
- Two LV checkout paths: the risk is already accepted. Just confirm both show up in reporting.

---

8. Weekly rhythm after launch (about 2 h a week for Sean)

- **Mon**: scorecard (15 min), approve the week's queue (15 min), W2SA proof post.
- **Tue**: paper teaser or snippet, plus an email every other week.
- **Wed**: carousel or snippet.
- **Thu**: paper launch and breakdown, or an evergreen recycle.
- **Fri**: snippet, queue next week, review the next paper.
- **Each paper runs on a 2-week cycle:**
  - Week A: teaser, then publish and breakdown.
  - Week B: snippet wave and carousel.
  - Then it gets an email CTA in the next email slot, and its best post is recycled about a month later.

---

9. Q4 calendar (pulled forward)

Q4 Content Calendar · Oct 12 – Dec 17, 2026

Pulled forward: P2 publish Oct 27 → Oct 22 · P3 created Oct 17 (was Oct 23) · Facebook live Oct 17 · email live 7 weeks before the Dec 10 push.

PAPER LAUNCHES	EMAIL SENDS
Oct 22 · Nov 5	5 planned

Decisions / ops · Social · W2SA mobile · Email · Billing · Papers · Tracking · Security · Gate / milestone

October 2026

MON	TUE	WED	THU	FRI	SAT	SUN
12	13	14 DECISIONS / OPS Decisions · Mailgun DNS · P2 generated	15 SOCIAL P1 announcement · W2SA phone fix	16 GATE / MILESTONE ★ Machine running · P1 carousel · security hour	17 PAPERS P3 created · Facebook page live	18 SOCIAL Week 1 queued · tunnel rotation
19 TRACKING Scorecard #1	20 SOCIAL ★ P1 snippet wave 1 · Email #1	21 PAPERS P2 teaser · P3 done	22 PAPERS P2 publish + breakdown	23	24	25
26 SOCIAL Scorecard · P2 snippet wave	27 SOCIAL P2 carousel	28	29 SOCIAL Evergreen paper recycle	30	31	

November 2026

MON	TUE	WED	THU	FRI	SAT	SUN
						1
2 TRACKING Scorecard	3 EMAIL P3 teaser · Email #2	4	5 PAPERS P3 publish + breakdown	6	7	8
9 SOCIAL Scorecard · P3 snippet wave	10 SOCIAL P3 carousel	11	12 SOCIAL P1 best-performer recycle	13	14	15
16 TRACKING Monthly review	17 EMAIL Email #3 — mid-quarter push (new)	18	19 SOCIAL Evergreen paper recycle	20	21	22
23 TRACKING Scorecard · light week	24	25	26 DECISIONS / OPS Thanksgiving — no posts	27	28	29
30 SOCIAL Scorecard · snippet wave 2 (P2/P3)						

December 2026

MON	TUE	WED	THU	FRI	SAT	SUN
	1 EMAIL Email #4	2	3	4	5	6
7 TRACKING Scorecard	8 SOCIAL Recap carousel: 3 papers, 15 takeaways	9	10 EMAIL ★ Email #5 — Dec 10 push (kept)	11	12	13
14 TRACKING Scorecard	15	16	17 GATE / MILESTONE ★ Q4 wrap · retro · Q1 plan	18	19	20
21	22	23	24	25	26	27
28	29	30	31			

Weekly rhythm after launch

about 2 hours a week of Sean's time

Mon
Scorecard (15m) · approve the week's queue · W2SA proof post

Tue
Paper teaser or snippet · email every other week

Wed
Carousel or snippet

Thu
Paper launch + breakdown, or evergreen recycle

Fri
Snippet · queue next week · review next paper

Source: Portfolio SITREP 2026-10-14. Generated by build/calendar.py from build/plan_data.py. Printable week-per-page version: calendar/launch-calendar-print.pdf.

Week of	Main moves
Oct 12	Decisions, Mailgun DNS, P2 generated (Wed). P1 announcement (Thu). ★ **Machine running**, P1 carousel, security hour (Fri). P3 created, Facebook live, paper keep/archive (Sat). Week 1 queued, tunnel token rotated, first Facebook post (Sun).
Oct 19	Scorecard #1 (Mon). ★ **P1 snippet wave 1 + email #1 (Tue 20).** P2 teaser, P3 final (Wed). **P2 publish (Thu 22).**
Oct 26	P2 snippet wave and carousel. Evergreen recycle. Email #2 drafted.
Nov 2	P3 teaser + email #2 (Tue). **P3 publish (Thu Nov 5).**
Nov 9	P3 snippet wave and carousel. Recycle P1's best performer.
Nov 16	Monthly review. **Email #3, mid-quarter push (new, Tue Nov 17).**
Nov 23	Thanksgiving week (Thu Nov 26): light, 2 scheduled posts.
Nov 30	Snippet wave 2 (P2/P3). Email #4 (Tue Dec 1).
Dec 7	Recap carousel: "3 papers, 15 takeaways" (Tue). ★ **Email #5, Dec 10 push (kept: year-end timing suits a "2027 readiness" offer).**
Dec 14	★ **Q4 wrap, retro, Q1 plan (Thu Dec 17).**

- **Print it:** `calendar/launch-calendar-print.pdf` has one week per landscape page, with a detail line and a checkbox for every item, plus a notes area.
- **Import the dates:** `calendar/launch-calendar.ics` has one all-day event per work day, with that day's tasks in the description. It works with Google Calendar (Settings → Import) or Apple Calendar.

---

10. Gate: "launched and marketing" (review Fri Oct 16, 16:00)

1. All three sites work on desktop and phones. W2SA, LV, and the P1 page pass the §7.2 real-phone checklist, including the LinkedIn in-app browser. The DBR CRM works on a phone for Sean.

2. Revenue is visible in one place. DBR shows dbr-api charges (W2SA and LV) and the brand-nexus W2SA charges (Option B). The weekly total matches Stripe.

3. At least one social channel posts on the calendar. The P1 announcement and carousel are live on LinkedIn, and next week's posts are queued.

4. The audit-offer email can go out. Either the Mailgun domain is verified, the template is tested, and unsubscribe works — or the 1:1 fallback is in progress.

5. Bookings and checkouts are tracked weekly. The scorecard exists with baseline numbers, and the first Monday review is Oct 19.

- Also confirmed this sprint:

- [ ] Live Stripe webhook healthy.
- [ ] No uncommitted work.
- [ ] Anthropic key rotated.

---

11. Risks & fallbacks

Risk	Early sign	Fallback
Mailgun DNS slow to verify	Not verified by Fri 12:00	Sean sends 1:1 emails from his inbox. The bulk send moves to Tue Oct 20 as planned.
Generator fix slips	Output still wrong on Thu	Keep writing posts by hand (already the Day 1 plan). The fix isn't needed until P2's pack.
Phone issues bigger than expected	Real-phone test fails on Thu	The hotfix (no intro on phones) already removes the main risk. Polish can follow.
Sean's time	Decisions or approvals stack up	Defaults apply at 9:00 the next day. D8 replaces per-post approval with one weekly queue approval.
Key rotation breaks n8n	A workflow fails after the switch	Don't revoke the old key until the new credential is proven (§7.7 order).
Live Stripe webhook unhealthy	Failed deliveries on Day 0	Stop and fix first, then resend the failed events from Stripe.
Company pages get little reach	Low impressions in week 1	Sean's personal profile is already the main channel, and Facebook is live from Oct 17.
Option B double-counts	Totals don't match Stripe	Match on Stripe object IDs and reconcile weekly.
P2 fails review	Big fixes needed	Use the Oct 22 slot for an evergreen paper from the 20-paper library. P2 takes the Nov 5 slot.

12. Parking lot (frozen or dormant — no action this sprint)

- **Frozen until the machine is running and the scorecard shows a trend:** LUVK v2 deploy, LUVK local-AI switch (waits for the new GPU PC), NCC, Amatrix/HRC Stripe accounts, the `dbr_projects` table, EASS judge wiring, the LV multi-tenant vault, NDRS, voice/narration, new Nexus agents.
- **Archive (D7):** SITREP Intelligence, Knowledge Engine, WP_Distribution video build.
- **Keep as frozen documents:** the HAWL, Amatrix, and HRC playbooks.
- **Out of scope:** Huladik (a separate brand).

Appendix A — P1 post templates

A1. Announcement + breakdown (LinkedIn, Sean's profile)

```
Most small-business websites aren't broken. They're quietly losing customers.

We just published The 2027 Small Business Digital Readiness Report.
Three findings stood out:

1) [Finding #1 — one line, with the number]
2) [Finding #2 — one line, with the number]
3) [Finding #3 — one line, with the number]

The pattern: [one-sentence "so what" for an owner].

Full report (free): [P1 link + UTM: utm_content=announce]

Want to know where your own site stands? W2SA runs a free
Digital Health Check — plain-English findings, no rebuild pitch:
[w2sa.online/digital-health-check + UTM]
```

A2. Snippet card (one per finding)

- **Card (1080×1350):**
  - The stat, large.
  - One line of context.
  - Source line: "2027 Small Business Digital Readiness Report · Lucent Veritas."
- **Post copy (2–3 lines):**
  - Why it matters to an owner.
  - A question for the reader.
  - A link to the free check (UTM `snippet-0N`).

A3. W2SA proof post (Mondays)

```
A website can look fine and still lose customers.

The most common problem we find: [e.g., the contact form fails on phones].
What it costs: [e.g., every mobile visitor who tries to reach you gives up].
The fix is usually small: [one line].

Free Digital Health Check: [link + UTM: utm_content=proof-0N]
```

Appendix B — Audit-offer email (W2SA, signed by Sean)

```
Subject: Is your website ready for 2027? (free check)
Preview: A 2-minute form. A plain-English answer.

Hi {first_name},

We just published The 2027 Small Business Digital Readiness Report
with Lucent Veritas. The short version: [one-line finding].

The most common problems we see aren't expensive to fix — they're
just invisible:
  • contact forms that fail on phones
  • not showing up in local search
  • the main "call us" button buried below the first screen

If you'd like to know where your site stands, we'll do a free
preliminary Digital Health Check. No rebuild pitch, no obligation.

→ Start my free check:
https://w2sa.online/digital-health-check?utm_source=email&utm_medium=email&utm_campaign=audit-
offer&utm_content=email-01

Sean
W2SA

[Postal address] · Unsubscribe: %unsubscribe_url%
```

Appendix C — Files in this folder

- `LAUNCH_PLAYBOOK.md`: this playbook.
- `LAUNCH_PLAYBOOK.pdf`: the same playbook as a PDF.
- `calendar/launch-calendar.html`: the visual calendar (sprint view and Q4 view). Open it in a browser.
- `calendar/sprint-calendar.png` and `calendar/q4-calendar.png`: the calendar as images.
- `calendar/launch-calendar-print.pdf`: the printable calendar, one week per landscape Letter page (10 pages).
- `calendar/launch-calendar-print.html`: the same printable calendar. It also prints from a browser (landscape, margins "None").
- `calendar/launch-calendar.ics`: one all-day event per work day, for Google or Apple Calendar.
- `assets/w2sa-mobile-baseline.png`: the phone-simulation screenshots.
- `build/plan_data.py`: the day-by-day plan that every calendar file is generated from.
- `build/`: rebuild everything with `bash build/build.sh` (needs Python 3, pandoc, Node, and Playwright).
